


Housing S/N <u>25I444-8</u> Plug S/N <u>MQ-7</u>

			REFERENCE			
OP	AREA	OPERATION DESCRIPTION	PROCEDURE	NAME	DATE	DR#
-			OR DRAWING	10 1111	D, (12	D/(//
	<u> </u>	Record I.D. Number of Superconducting	I			
10	46	Cable: 4Hc-3-A-A/00/12 Include copy of		_ ,		
'0	10	certs in Appendix A		1-Bish	12/10/02	
		Cut 4 S/C cable pieces to length, tinning	J. Zbasnik sketch, "Rutherford Cable for MQX1"	. /	10,000	
	:	lends with Stay-Bright Solder.Punch I.d.	J. Zbasnik sketch,			
20	46	hole in both ends, mark thin edge with Red	"Rutherford Cable	Pnil	11	
		marker	for MQX1"	1.0mg	2/20/03	
-		Record I.D. Number of			<i>,</i> -	
30	46	Copper Cable: 4Hc-Ass 37-9318 Include		00.4		
30	40	copy of certs in Appendix A		P-Bish	12/10/02	
		Copy of Certs III Appelluix A			1.70	****
		Cut 4 Cu cable pieces to length, tinning	J. Zbasnik sketch,			
40	46	ends with Stay-Bright Solder. Mark thick	"Rutherford Cable	P. Brist	2/2/20	
		edge with Blue marker	for MQX1"	("Drug	2/21/03	
		Separately tin areas with 60/40 Sn Pb			-	
		solder as required. Check that proper	J. Zbasnik sketch,			
50	46	solder is used PB;	"Rutherford Cable for MQX1"	Pail	2/28/03	
		check that proper flux is used	for MQX1"	r-Brus	9 28103	
		Solder fill area for lambda plug seal with				
		60/40 Sn Pb solder, check that blue and	J. Zbasnik sketch,			
60	46	red marks are together PR;	"Rutherford Cable	į		
	'	check that proper solder is used B;	for MQX1"		11	
		check that proper flux is used DB	10. 11.00	(Bish	3/4/03	
70	46	Join pretinned areas as required.		PBish	2/4/01	
		Send cables to plating shop for flux		7,0,000	3/1/02	
80	46	removal and cleaning		Y Bish	3/6/03	
90	46	Bakeout cables at 80 C to remove water		PRick	2/2/03	
400	40	Grit blast lambda plug seal area, acetone			7 // .	
100	46	and alcohol rinse		E-Broil	3/10/03	
		Apply Kapton wrap on each side of plug	1 7	10000	///	
110	40	seal area: check that Kapton film is .002 "	J. Zbasnik sketch,	1		
110	46	thk x 0.315" wide <u>PB</u> .	"Rutherford Cable		, ,	
		Apply two layers, each with 50% overlap.	for MQX1"	C. Lu	3/13/00	
120	46	Hold in clean, dry storage for potting		Cole	3/18/10	
		Record I.D. Number of Corrector Bus:			1.10	
130	46	Include copy of certs				
		in Appendix A				
			1	·	L	






Housing S/N 251448-8 Plug S/N MQ-7

ОР	AREA	OPERATION DESCRIPTION	REFERENCE PROCEDURE OR DRAWING	NAME	DATE	DR#
140	46	Cut 24 corrector bus pieces to length	J. Zbasnik sketch, "Corrector Bus for MQX1"	P-Brail	4/16/03	
150	46	Remove baked-on Kapton insulation	J. Zbasnik sketch, "Corrector Bus for MQX1"	C. Lee	4/22/03	
160	46	Grit blast lambda plug seal area, acetone and alcohol rinse		P. Bris	4/22/03	
170	46	Prepare G-10 CR Plug for potting. <i>Include</i> copy of certs in Appendix A	Procedure Needed	P.Bish	5/20/03	
180	46	Insert Conductors in G-10 Plug		C. Lee	8/20/03	
190	46	Verify Proper Orientation of Conductors; witnessed by:	S/C cables face corrector bus array	P. Bish	5/21/03	
200	46	Mix 200 g of Stycast 2850MT(blue), 10 g of 24 LV Hardener, 6 drops of Antifoam 88 witnessed by:		P-Bish &Bish	5/28/03	·
210	46	Seal conductors per procedure	Procedure Needed	8 Bich	5/28/03	
220	46	Reserve excess epoxy for archival sample. When cured, measure durometer hardness; Durometer = <u>90</u>		P-Bral		
230	46	Prepare for injection in vacuum chamber	Procedure Needed	P.Brish	5/29/03	
240	46	Mix 500 g of Stycast 2850MT(blue), 25 g of 24 LV Hardener, 15 drops of Antifoam 88 witnessed by:		P-Bish P-Bish	5/20/03	
250	46	Perform injection per procedure	Procedure Needed	P-Bick	5/30/03	






Housing S/N 251448-8 Plug S/N Ma-7

ОР	AREA	OPERATION DESCRIPTION	REFERENCE PROCEDURE OR DRAWING	NAME	DATE	DR#
260	46	Reserve excess epoxy for archival sample. When cured, measure durometer hardness; Durometer = 90	Procedure Needed	P.Bish	6/2/03	
270	46	Dunk plug in LN 3 times	Procedure Needed	P-Bish	6/10/03	
280	46	Vacuum leak test after warming and drying; B.S. 1.5x10-9 No Helium PLt. Leak rate = 4.S. 4.5x10-6 Leak atm cc/s 3x10-5 Me	Procedure Needed	P-Brish	6/11/03	
290	46	Hipot cond to cond to 5 kV, Passed Hipot? Yes : No 7.5 kV on worder. Include data sheet in Appendix B . O. O. A.	lud Procedure Needed Led A	Mal	6/17/13	
295	46	Holo for Engineer Approval to proceed		/		
300	46	Prepare SS Plousing for potting Make sure S/N of housing matches S/N in this Traveler Include copy of certs in Appendix A	Procedure Needed	P-Bish	6/18/03	
310	46	Prepare G-10CR plug/bus assembly for potting	Procedure Needed	P-Bish	6/18/03	
320	46	Insert Plug into housing in vacuum chamber to allow magnet side (pipe end) potting		P.Bish	6/18/03	
330	46	Mix 200 g of Stycast 2850MT(blue), 10 g of 24 LV Hardener, 6 drops of Antifoam 88 witnessed by: _M Include copy of certs in Appendix A		P-Bist	6/19/03	
340	46	Pot per procedure	Procedure Needed	P-Bish	6/19/02	
350	46	Reserve excess epoxy for archival sample. When cured, measure durometer hardness; Durometer =				
360	46	Position assembly in vacuum chamber for potting the DFBX side (flange end)		P-Bril	6/20/03	





Housing S/N 251448-8 Plug S/N MB-7

				· · · · · · · · · · · · · · · · · · ·		
OD	٨٥٣٨	ODED ATION DESCRIPTION	REFERENCE	NIA BAF	DATE	20 4
OP	AREA	OPERATION DESCRIPTION	PROCEDURE	NAME	DATE	DR#
			OR DRAWING			
		Mix 300 g of Stycast 2850MT(blue),				
		15 g of 24 LV Hardener,				
370	46	9 drops of Antifoam 88 witnessed				
		by: M.6.				
		Include copy of certs in Appendix A		Y-Rail	6/20/2	
380	46	Pot per procedure		Q dist	10015	
360	40	Pot per procedure		1.000	6120108	
		Reserve excess epoxy for archival sample.			,	
390	46	When cured, measure durometer				
	"	hardness; Durometer =				
		mardness, Burometer –				
400	4.0	Dunle when in 1 N 2 times	Procedure	On 1	-1-1	
400	46	Dunk plug in LN 3 times	Needed	Y-Brok	7/15/03	
		Vacuum leak test after warming and	December		//	·
410	46	drying, using Test Assembly 25M905	Procedure	00	-/-/	••
		drying, using Test Assembly 25M905 mbm Leak rate = \(\)\(\)\(\)\(\)\(\)\(\)\(\)\(Needed	1-Biss	7/18/03	
420	46	Package and ship to B77, include traveler		001	1/1/	
420	46	for work completed thus far		Y-Brish	7/18/03	
	-	I are a second and the second are a second are a second and the second are a second are		<u> </u>	119/52	

ENGINEERING NOTE

Author

Jon Zbasnik

Cat. Code LH2003

Serial #

Page

10 of 12

Department

Mechanical Engineering

Date **6 June 2003**

Date:	Helium Leak Rate:		Signed:
	ctor Protection Tube? Yes		
Witnessed:			
g. OP 760 (MBX1), OP xxx	x (MQX1): Lambda Plug Leak	Check after	r LN Temperature Pressure Test
maximum leak rate that can Follow the steps in g.1 if the	be measured with a conventional leak rate can be measured with a	al helium ma a convention	cc/sec (helium), which exceeds the ass-spectrometer type leak detector all leak detector. If the leak rate surement in g.2.
g.1 Leak Detector Method Remove the Conductor Prot assembly as in part IV-a abo Measure and record the roor	ection Tube and connect a helium ove. Apply a spray of Helium gas n temperature leak rate.	n mass spect to the expos	rometer leak detector to the sed conductors.
Date:	Helium Leak Rate:		Signed:
Witnessed:			
g.2 Rate of Pressure Rise N	5/N. 25 Method	IU48	-8-mg-7
Make sure the Conductor Pr Evacuate the piping to about Close the Veeco valve and re Allow the pressure to rise to Note: The trapped volume is	ecord the reading of the convectr	i vacuum ga nosphere. on gage ever	uge on the other leg.
Date: <u>8/8/03</u>			
Time: 8-25 Time: 8-26 Time: 8-27 Time: 8-28 Time: 8-29	Pressure: 24 M. Torr Pressure: 408 M. Torr Pressure: 408 M. Torr Pressure: 594 M. Torr Pressure: 482 M. Torr		

ENGINEERING NOTE

Cat. Code LH2003

Serial #

Page **11 of 12**

Date

Author

Jon Zbasnik

Department

Mechanical Engineering

6 June 2003

Time: 8:30	Pressure: 975-M-TOW
Time: \$.31	Pressure: 1. Tory
Time: 8:32	Pressure: 1. Torr
Time: 8,33	Pressure: 2.70m
Time: 8.34	Pressure: 2. Torr
Time: 8:55	Pressure: 2 TOVY
Time: 8.36	Pressure: 2.7011
Time: 8:37	Pressure: 2.70rr
Time: 8738	Pressure: 2 TOIY
Time: <u>\$.24</u>	Pressure: 3 Tors
Signed: AMWet Pa	heds
Witnessed:	

h. OP 770 (MBX1), OP xxx (MQX1): Lambda Plug Leak Check after LN Temperature Pressure Test

Install a "Rad-Lab" Tee to the Conflat Flange on the end of thie Conductor Protection Tube.

Connect one leg of the Tee to a pumping station through a Veeco-style vacuum valve and install a Convectron vacuum gauge on the other leg.

Make sure the Helicoflex flnage is opened to the atmosphere.

Evacuate the Conductor Protection Tube to about 20 mTorr.


Close the Veeco valve and record the reading of the convectron gage every 60 sec.

Allow the pressure to rise to about 10 Torr.

Note: The trapped volume for MBX1 is 4.3 liter, so the rate of pressure rise must be less than 6.5 mTorr/sec, and the trapped volume for MQX1 is 8.3 liter, so the rate of pressure rise must be less than 3.4 mTorr/sec.

Date: _		
	Time:	Pressure:






Housing S/N 251448-8 Plug S/N MB-7

Note: Add S/N at OP 300 See last page for signoffs

ОР	AREA	OPERATION DESCRIPTION	REFERENCE PROCEDURE OR DRAWING	NAME	DATE	DR#
430	77	Remove Protective Assembly 25M951 from conductors and install the lambda plate housing in the assembly fixture	·	P. Bish	8/18/03	- 1
440	77	Rotate lambda plug to proper orientation		P.Bish	8/18/02	
450	• 77				10/10	
460	77	Make Bend 1 of the 28-conductor bundle		8.Bisl	8/18/03	
470	77			,	77	
480	77				-	
490	77	Make the 5-inch-long solder joints for current transfer in the inner and outer cables. Verify that 60/40 Sn/Pb solder is used. Verify that rosin-type flux is used. Clean any flux residue after soldering.		P-Brist	<i>ह</i> 19/13	
500	77	Apply Kapton wrap on cable bus #1, overlapping existing Kapton wrap by at least 1.5 inch; check that Kapton film is .002 " thk x 0.315" wide Apply two layers, each with 50% overlap.		P-Brish	3/19/03	
505	77	Apply Kapton wrap on cable bus #2, overlapping existing Kapton wrap by at least 1.5 inch; check that Kapton film is .002 " thk x 0.315" wide Apply two layers, each with 50% overlap.		P.Breh P.Breh	8/19/03	
510	77	Apply Kapton wrap on cable bus #3, overlapping existing Kapton wrap by at least 1.5 inch; check that Kapton film is .002 " thk x 0.315" wide Apply two layers, each with 50% overlap.		P.Dish	<u> </u>	
515		Apply Kapton wrap on cable bus #4, overlapping existing Kapton wrap by at least 1.5 inch; check that Kapton film is .002 " thk x 0.315" wide Apply two layers, each with 50% overlap.		P-Brish	8/19/03	
520		Install fishbone G-10 spacers beween cable conductors in the straight section. Use 14 inch long pieces.		P.B.ist	8/20/22	
530	77	Install strip insulators between corrector busses in the straight section. Use 14 inch long pieces.		P.Brish P-Brish	8/20/03	

B46 ver. April 24, 2003 B77 ver. July 30, 2003






Housing S/N 257448-8 Plug S/N MR-7

	1				 	
OP	AREA	OPERATION DESCRIPTION	REFERENCE PROCEDURE	NAME	DATE	DR#
	 		OR DRAWING			
		Apply Kapton ground wrap over the bus				
540	77	assembly straight section; check that		1		
340	77	Kapton film is .002 " thk x 0.315" wide Apply two		00 1		
		1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1		P-Brist	8/20/03	
		layers, each with 50% overlap.	*	*.	, , ,	
550	77	Apply spiral wrap of Kevlar tape over the Kapton ground wrap. 1/4 inch pitch. Epoxy		01	,	
	''	the starting and stopping knots.		P-Brish	1/20/02	
		Slip the large radius elbow, with backing		•	0/00/0	
		rings attached, into position. Clamp into		Poss		
555	77	position. Include a copy of the certs in		Pos us	plantan	
		Appendix A.		10000	012903	
		Install 2 G-10 spiders, 25M937, in the				
		straight section as shown on 25M857.				
560	77	Apply a wrapping of fiberglass tape,				
		soaked with epoxy, on both sides of the		P.Bish	8/00/01	
		spiders to keep them in position.		(),,,,,	0/00/02	
		Install Vertical Pipe assembly 25M908.		*****		
		Note: this subassembly must have		_		
570	77	previously been thermally shocked and		P. Bish	0/2/2	
		leak checked. Include a copy of the		1-222	0 100	
		testing report in Appendix B.				
		Bend the conductors to form the second				
-00		bend and clamp in position. Insert strip and				
580	77	fishbone insulators between conductors		Qn .1	0/-/-	
		and extend 1.5 inch past the horizontal		P-Brisk	8/21/03	
590	77	elbow weld.				
600	77					
000		Apply Kapton ground wrap to the end of				
		the 1.5 inch-long section with G-10	Ī			
610	77	insulators; check that Kapton film is .002 "			, ,	
	• •	thk x 0.315" wide		Y-Rush	\$/21/09	
		Apply two layers, each with 50% overlap.		P-Bist	100	
		Apply spiral wrap of Kevlar tape over the				
620	77	Kapton ground wrap. 1/4 inch pitch. Epoxy			0/./.	
		the starting and stopping knots.		Y-13roh	0/21/03	
		Slip the small radius elbow, with backing				
625	77	rings attached, into position. Clamp into		Qn -1	01-1-	
		position		P.Brah	3/M/03/	
			<u> </u>		4 -	






Housing S/N 252448-8 Plug S/N Ma-7

Note: Add S/N at OP 300 See last page for signoffs

		T				
OP	AREA	ov Environ Bedomin Hom	REFERENCE PROCEDURE OR DRAWING	NAME	DATE	DR#
630	77	Install 1 G-10 spider as shown on 25M857. Apply a wrapping of fiberglass tape, soaked with epoxy, on both sides of the spider to keep it in position.		P-Brish A.Rekedis	8/21/03	
640	77	Install Horizontal Assembly 25M907. Note: the bellows in this subassembly must have previously been thermally shocked and leak checked. Include a copy of the testing report in Appendix B.		A. Reliedis	रीरग०५	
645	77	Perform closeout welding. Use GTAW process, with a skipping technique and intermediate cooling with "cool gun" to minimize heat input. Fill out weld log and include in Appendix C.				
647	77	Dimensional Check of Bus Duct Piping within tolerance? Yes _ 🔀 No		A. P		
650	77	Adjust bellows to the proper length. Trim conductors to a 5.75 inch overhang out of 25M907. Make sure the cable end is tinned with Stay Bright solder before cutting to prevent the cable from unravelling.		A.P.		
655	77	Ring out conductors and attach labels to conductors. Include data sheet in Appendix B	MQX1 Electrical Test Procedure			
660	77	Place teflon tubes over the individual conductors to prevent end flashover during hipot testing. Teflon tubes to extend from the section with G-10 insulators 1.5 inch past the end. Wrap with mylar tape to hold the tubes in place.		A.P.		
665	77	Install Spacer 25M956 as shown on 25M857.		A.P.		
670		Install Test Cap 25M950. Note: this subassembly must have previously been thermally shocked and leak checked. Include a copy of the testing report in Appendix B.		A. P.		
680	77					
690	77					

B46 ver. April 24, 2003 B77 ver. July 30, 2003






Housing S/N 257448-8 | Plug S/N MQ-7

Note: Add S/N at OP 300 See last page for signoffs

	1			 	T	
OP	AREA	OPERATION DESCRIPTION	REFERENCE PROCEDURE	NANAE	DATE	DD 2
•	''''	CI ELIVITON BEGOLILI FION	OR DRAWING	NAME	DATE	DR#
			ONDINAWING	 		
700		Leak check closeout welds. Connect to		A. P.	9/11/03	
700	77	ISO flange on 25M908. Leak rate less		'' '	,	
		than 1 x 10 ⁻⁹ atm cc/s (helium) ? Yes				
		Dunk assembly in LN 2 times to thermally		2 0	0/ -1	
710	77	shock closeout welds. Use dry Ne gas	•	AP.	9/15/03	
		inside piping.				
		Pressure test closeout welds & lambda		A.P	9/11/2	
720	77	plug at room temperature to 370 psig with	Procedure	17 · 1	9/16/03	•
		dry N ₂ Include data sheet in Appendix B.	needed		:	
<u> </u>						
730	77	Leak check closeout welds. Leak rate less		$ \Delta D $	9/16/03	
	,,	than 1 x 10 ⁻⁹ atm cc/s (helium) ? Yes <u>V</u>		15-1.	,,,,,,,	
					61.	
740	77	Pressure test closeout welds and lambda	Procedure	H.V.	9/17/03	
740	77	plug at LN temperature to 370 psig with dry	needed			
		N _{e.} Include data sheet in Appendix B.			İ	
		Leak check closeout welds. Leak rate less		A.P.	aludos	
750	77	than 1 x 10 ⁻⁹ atm cc/s (helium) ? Yes		17.7.	9/16/03	
		Determine leak rate or rate of rise across		AP	9/19/03	
760	77	lambda plug from flange side to pipe side.		13.4.	1117/07	
		Leak rate less than 0.1 atm cc/s? Yes NO				
		Determine leak rate or rate of rise across				
770		lambda plug from pipe side to flange side.				
770	77	Leak rate less than 0.1 atm cc/s?				
		Yes				
780	77	Attach "pressure-tested" label to magnet		C.L.	1/6/ 11	
		end of the assembly		C, L,	1/9/04	
790	77	Hipot cond to cond to FIM is air Day				
800	77	Hipot cond to cond to 5 kV in air, Passed Hipot? Yes No				
	''	Include data sheet in Appendix B				
		Hipot cond to cond to 2 kV in He, Passed				
810		Hipot? Yes No				
		Include data sheet in Appendix B				
820	77					

B46 ver. April 24, 2003 B77 ver. July 30, 2003





Housing S/N 25T 448-8 Plug S/N MB-7

ОР	AREA	OPERATION DESCRIPTION	REFERENCE PROCEDURE OR DRAWING	NAME	DATE	DR#
830	77	Cover the conductor bundle with a close-fitting teflon tube. Attach spacers 25M955 on the bundle as shown on 25M857 to prevent the bundle from movement inside the tube.		Cita	1-9-04	
840	77	Install protective tube assembly 25M951. Flush both sides of lambda plug with dry N_2 gas and cap for shipment to DFBX vendor.		CE	1-9-04	
850	77	Package for shipment to DFBX vendor. Include a copy of the assembly's traveler in the shipping container.		CZ_	1-9-04	

Traveler Entries Reviewed by:		Date
,	Jon Zbasnik	
Traveler Approved by:	Joseph Rasson	Date

ENGINEERING NOTE

Cat. Code LH2003

Serial #

Page 1 of 12

Author

Jon Zbasnik

Department

Mechanical Engineering

Date 6 June 2003

Project:

LHC I.R. Feedboxes

Title:

Pressure and Leak Testing of MBX1 and MQX1 Bus Ducts

Part Serial Number 251448

I. Description

We present the thermal cycling and subsequent pressure and leak test of MBX1 and MQX1 Bus Ducts fabricated at LBNL. These assemblies contain superconducting busses that allow the superconducting inner triplet magnets and corrector magnets to be supplied with current. A barrier between the 1.8K, 1 bar superfluid helium magnet bath and the 4.3K, 1.3 bar liquid helium bath in the DFBX (lambda plug) is integral to the bus duct assembly.

Isometric views of MBX1 and MQX1 are shown in Figures 1 and 2, respectively.

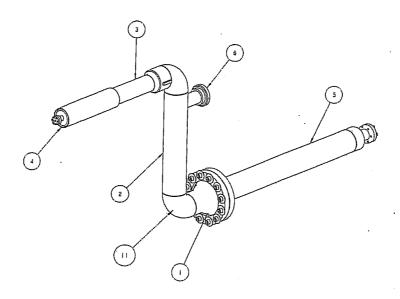


Figure 1. Isometric view of MBX1. 1-Housing with Lambda Plug; 2-Vertical Pipe Section; 3-Horizontal Section (this connects to magnet); 4-test Cap (this is removed for tunnel installation); 5-Conductor Protection Tube (this is removed for attachment to DFBX); 6-Helicoflex Sealing system; 11-Short Radius 3 IPS Weld Elbow.

am Euroratory - Omycratty of California

ENGINEERING NOTE

Author Jon Zbasnik

Cat. Code LH2003

Serial # XXXXXX Page 2 of 12

Department

Mechanical Engineering

Date 6 June 2003

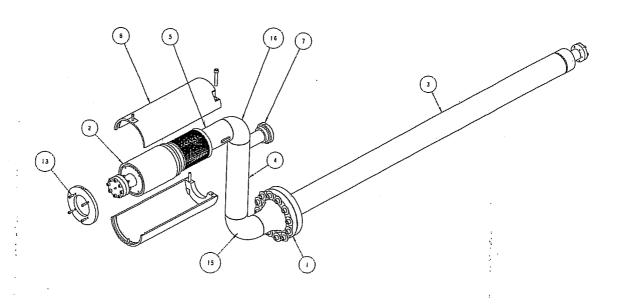


Figure 2. Isometric View of MQX1. 1 - Housing with Lambda Plug; 2 - Test Cap (this is removed for tunnel installation); 3 - Conductor Protection Tube (this is removed for attachment to DFBX); 4 -Vertical Pipe Section; 5 - Horizontal Section (this connects to magnet); 6 & 13 - Bellows Restraint (this is removed for tunnel installation); 7 - Helicoflex Sealing System; 15 - Long Radius 3 IPS Weld Elbow; 16 -Short Radius 3 IPS Weld Elbow.

The bus duct design pressure is 20 bar applied to the magnet side and 3.5 bar applied to the DFBX side. The duct would probably be damaged with hydrostatic testing using water since the electrical insulation would be compromised, so it will be tested pneumatically with dry nitrogen or helium. In accordance with Pub 3000, the magnet-side piping will be pressure tested to 25 bar (370 psig).

The magnet-side piping is 3 IPS (3.5 inch outer diameter) schedule 10, type 304L stainless steel pipe and weld elbows. The Lambda Plug housing is machined from a forged 304L stainless steel special weldneck flange. Welding was performed by LBNL welders using the GTAW process with ER316L filler wire. The assembly of NEMA G-10CR and conductors potted into the housing completes the pressure boundary of the magnet-side piping.

ENGINEERING NOTE

.

Serial #

Page 3 of 12

Author Jon Zbasnik

Department

Cat. Code

LH2003

Date

Mechanical Engineering

6 June 2003

II. Pressure Test Hazards

The chief hazard in this test is the stored energy in the pressurized gas providing a driving force that could eject the potted plug out of the housing.

The stored energy is given by:

$$U = \frac{P_h V_h}{\gamma - 1} \left[1 - \left(\frac{P_l}{P_h} \right)^{\frac{\gamma - 1}{\gamma}} \right],$$

where U = stored energy in N-m (J)

 P_h = Initial Vessel Pressure (absolute) in N/m² (Pa) = 25 bar = 2.5 MPa

 P_I = Final Vessel Pressure (absolute) in N/m² (Pa) = 0.1 MPa

 $V_h = \text{Vessel Volume in m}^3 = 442 \text{ in}^3 = 7.2 \times 10^{-3} \text{ m}^3$

 γ = specific heat ratio, C_P/C_V , = 1.67 for helium and 1.4 for nitrogen.

If we test with dry nitrogen,

$$U = \frac{3.0x10^6 * 7.2x10^{-3}}{1.4 - 1} \left[1 - \left(\frac{.1}{2.5} \right)^{\frac{1.4 - 1}{1.4}} \right]$$

$$U = 5.4x10^{4} \left[1 - (.04)^{.286} \right]$$

$$U = 3.25 \times 10^4 \text{ N-m or } 32 \text{ kJ}$$

The stored energy is quite low, and is equivalent to about 7.9 g of TNT.

If we test with helium,

$$U = \frac{3.0x10^6 * 7.2x10^{-3}}{1.67 - 1} \left[1 - \left(\frac{.1}{2.5} \right)^{\frac{1.67 - 1}{1.67}} \right]$$

$$U = 3.22x10^{4} \left[1 - (.04)^{401} \right]$$

$$U = 2.3 \times 10^4 \text{ N-m or } 23 \text{ kJ}$$

Dawlence Delkeley Ivanional Laboratory - University of California

ENGINEERING NOTE

Author Jon Zbasnik

Cat. Code LH2003

Serial #

Page 4 of 12

Department

Mechanical Engineering

Date **6 June 2003**

The stored energy is quite low, and is equivalent to about 5.8 g of TNT.

In spite of the rather low stored energies, the part should be tested behind a protective barricade such as inside a 1-inch-thick plywood box. The box should be large enough to accommodate the styrofoam dewar for cold pressure testing. The corners should be reinforced with 2 inch Al angle. The top should be easily removable to allow the part to be placed inside. The high pressure line and LN fill tube can also penetrate through the top.

III. Calculations

Allowable pressure in 3 inch pipe, fittings, and welds.

Assume full penetration welds, without Radiographic Testing. The allowable pressure in psi is given by:

$$P = \frac{SEt}{R + .6t},$$

where S = allowable stress (psi) = 16,500 psi

E = Joint Efficiency = .65 because of the welds

R = inner radius = 1.63

t = wall thickness (inch) = .12 inch

$$P_{allowable} = 756 psig$$

The test pressure of 370 psig is considerably below the allowable pressure of 756 psig.

Shear Stress in Stycast 2850MT bond between 304 Stainless Steel and the G-10CR Insulator block. We take the limiting case that the entire pressure load is carried by the Stycast epoxy bond between the stainless housing and the G-10CR insulator block,

$$\tau_{shear} = \frac{PA_{pipe}}{A_{shear}}$$

$$\tau_{epoxy} = P \frac{\pi r_i^2}{2\pi r_{G-10} l_{epoxy}},$$

where P = test pressure = 370 psig

 $r_i = inner radius of piping = 1.63 inch$

 r_{G-10} = outer radius of G-10CR insulator = 1.35 inch

 $l_{epoxy} = length of epoxy bond = 1.75 inch$

$$\tau_{epoxy} = 370x \frac{1.63^2}{2*1.35*1.75}$$

$$\tau_{epoxy} = 208 psi$$

LH2003

YYYYYY

5 of 12

Author

Jon Zbasnik

Department

Date

Mechanical Engineering

6 June 2003

Shear Stress in NEMA G-10CR Plug

In this case we have the limiting case in which the pressure load is carried by a shear load in the end of the G-10 insulator block.

$$\tau_{G-10} = P \frac{\pi r_i^2}{2\pi r_{G-10} * l_{G-10}}$$

where P = test pressure = 370 psig

 r_i = inner radius of piping = 1.63 inch

 r_{G-10*} = outer radius of G-10CR insulator joint = 1.1 inch

 l_{G-10} = shear length of G-10CR = .25 inch

$$\tau_{G-10} = 370 \frac{1.63^2}{2*1.1*.25}$$

$$\tau_{G-10} = 1787 \, psi$$

These shears are very low and are well within the materials' capability.

IV. Pressure & Leak Testing

a. OP 700 (MBX1), OP xxx (MQX1): Post-Weld Leak Check

Connect a calibrated helium mass spectrometer leak detector to Item 6, Figure 1 for the MBX1 or to Item 7, Figure 2 for the MQX1 and leak check the closeout welds using a tracer probe method in which helium in sprayed over the weld joints. The leak rate should be less than 1×10^{-9} atm cc/sec (helium).

The maximum acceptable room temperature helium leak rate for the lambda plug is 0.1 atm cc/sec (helium), which exceeds the maximum leak rate that can be measured with a conventional helium mass-spectrometer type leak detector. If the lambda plug leak rate is too high for the leak detector, pump in parallel on the Conductor Protection Tube to allow the leak detector to be used.

Cat. Code **LH2003** Serial#

XXXXXX

Page

Date

6 of 12

Author

Jon Zbasnik

Department

Mechanical Engineering

6 June 2003

b. OP 710 (MBX1), OP xxx (MQX1): Thermal Shock to LN Temperature

Make sure a teflon Oring is used to seal the Protection tube to the Lambda Plug Housing.

Pressurize both sides of the assembly shown in Figure 1 or Figure 2 to 20 psig with pure neon gas, valve the gas supply off and submerge the assembly in a bath of Liquid Nitrogen.

Hold in the LN bath for at least 1 hour to allow the part to reach LN temperature.

Remove from Liquid Nitrogen bath and allow the part to reach room temperature. Set up a fan to circulate a flow of air over the part and speed the warmup. Allow sufficient time for the part to defrost and become dry. Repeat the process to obtain 2 thermal cycles.

Signed: A Must behadis 9/12-9/15/03

Witnessed:

9/15/03

c. OP 720 (MBX1), OP xxx (MQX1): Room Temperature Pressure Test

The pressure test is to be performed using dry nitrogen gas.

Hook up dry nitrogen gas source to the magnet side piping as indicated in Figure 3.

Use pressure safety manifold M8104-6 with a relief valve set to 500 psig.

Allow any leakage across the lambda plate to be vented out the Conductor Protection Tube.

Place the part in the protective barrier described above.

Raise the pressure to 370 psig in steps of about 50 psi. Pause at each step for 60 sec. When 370 psig is attained, close the shutoff valve and record the test gauge reading for 10 minutes at 1 minute intervals.

Reduce pressure to 0 psig.

Cal. Coup LH2003

ochai # XXXXXX rage 7 of 12

Date

Department

6 June 2003

Jon Zbasnik

Author

Mechanical Engineering

Test Gauge Lambda Pl Regulator Vent MBX1 or MQX1 Dry Nitrogen

Figure 3. Pressure Test Setup.

Date: 9/16/02		
Time: 11:15 Am Time: 11:14 Time: 11:18 Time: 11:19 Time: 11:20 Time: 11:21 Time: 11:22 Time: 11:24 Time: 11:25	Pressure:	
Signade Alexand A	1 .	<i>y</i> =====

Witnessed:

d. OP 730 (MBX1), OP xxx (MQX1): Leak Check after Room Temperature Pressure Test

do Berkeley Ivanonal Laboratory - University of California

ENGINEERING NOTE

Author Jon Zbasnik

Cat. Code LH2003

Serial # XXXXXX Page

8 of 12

Department

Mechanical Engineering

Date 6 June 2003

Connect a calibrated helium mass spectrometer leak detector to Item 6, Figure 1 for the MBX1 or to Item 7, Figure 2 for the MQX1 and leak check the closeout welds using a tracer probe method in which helium in sprayed over the weld joints. The leak rate should be less than 1x10⁻⁹ atm cc/sec (helium).

The maximum acceptable room temperature helium leak rate for the lambda plug is 0.1 atm cc/sec (helium), which exceeds the maximum leak rate that can be measured with a conventional helium mass-spectrometer type leak detector. If the lambda plug leak rate is too high for the leak detector, pump in parallel on the Conductor Protection Tube to allow the leak detector to be used.

Bacarond 2.8x10-10 Atm Casec-He
Date: 1/16/03 Helium Leak Rate: 1 No Responsigned: 11 Mot fluels
Parallel Pumping on Conductor Protection Tube? Yes No
Witnessed:

13. Page 11. e. OP 740 (MBX1), OP xxx (MQX1): Pressure Test at LN Temperature

The pressure test is to be performed using neon gas.

Hook up the neon gas source to the Assembly as indicated in Figure 4.

Use pressure safety manifold M8104-6 with a relief valve set to 500 psig.

Allow any leakage across the lambda plate to be vented out the Conductor Protection Tube through a relief valve set to 30 psig The relief valve is at room temperature.

Place the part in the protective barrier described above.

Raise the pressure to 370 psig in steps of about 50 psi. Pause at each step for 60 sec. Maintain at 370 psig for 10 minutes.

Reduce pressure to 0 psig.

Allow the assembly to reach room temperature

ENGINEERING NOTE

Author

Jon Zbasnik

Cat. Code LH2003

Serial #

Page 9 of 12

Department

Mechanical Engineering

Date

6 June 2003

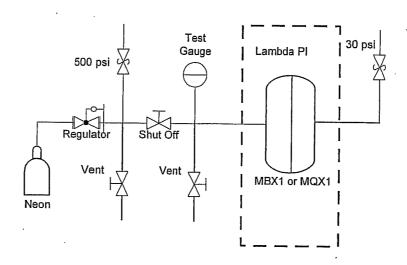


Figure 4. LN Temperature Pressure Test Setup.

Date: 4/17/03

Time: 10:00 AM Pressure at 370 psig

Time: 11:10 Au Pressure released to 0 psig

Signed:

Witnessed:

f. OP 750 (MBX1), OP xxx (MQX1): Leak Check after LN Temperature Pressure Test

Connect a calibrated helium mass spectrometer leak detector to Item 6, Figure 1 for the MBX1 or to Item 7, Figure 2 for the MQX1 and leak check the closeout welds using a tracer probe method in which helium in sprayed over the weld joints. The leak rate should be less than 1x10⁻⁹ atm cc/sec (helium).

The maximum acceptable room temperature helium leak rate for the lambda plug is 0.1 atm cc/sec (helium), which exceeds the maximum leak rate that can be measured with a conventional helium mass-spectrometer type leak detector. If the lambda plug leak rate is too high for the leak detector, pump in parallel on the Conductor Protection Tube to allow the leak detector to be used.

ENGINEERING NOTE	Cat. Code LH2003	Serial #	Page 10 of 12
Author Jon Zbasnik	Department Mechanical	Engineering	Date 6 June 2003
Buckround 2.6×10-10 ATM	colbectte	2	
Date: 9/18/03 Helium Leak Rate: 6N0	Response	Signed:	met fekede
Parallel Pumping on Conductor Protection Tube? Yes	No		
Witnessed:	•		
g. OP 760 (MBX1), OP xxx (MQX1): Lambda Plug Le	ak Check afte	r LN Tempera	nture Pressure Test
The maximum acceptable helium leak rate for the lambda maximum leak rate that can be measured with a convention Follow the steps in g.1 if the leak rate can be measured with cannot be measured with a mass spectrometer, perform a reg.1 Leak Detector Method Remove the Conductor Protection Tube and connect a heliansembly as in part IV-a above. Apply a spray of Helium & Measure and record the room temperature leak rate.	onal helium manth a convention rate of rise mea	ass-spectrometer al leak detector surement in g.2	er type leak detector. or. If the leak rate 2.
Date: Helium Leak Rate:		Signed:	•
Witnessed:			
g.2 Rate of Pressure Rise Method			
Install a "Rad-Lab" Tee to the Helicoflex Seal Flange. Conthrough a Veeco-style vacuum valve and install a Convect Make sure the Conductor Protection Tube is opened to the Evacuate the piping to about 20 mTorr. Close the Veeco valve and record the reading of the convect Allow the pressure to rise to about 10 Torr. Note: The trapped volume is 7.2 liter, so the rate of pressure.	on vacuum gau atmosphere. etron gage ever	nge on the othe	r leg.

Date: <u>9/19/03</u>

Time: 11: 47

Pressure: 105 M.T

Time: 11: 48

Pressure: 1.2 Tolv

Time: 11: 50

Pressure: 4. Tolv

Time: 11: 51

Pressure: 5.2 Tolv

Lawrence Berkeley National Laboratory - University of California ENGINEERING NOTE Author Jon Zbasnik	Cat. Code LH2003 Department Mechanical	Serial # XXXXXX Engineering	Page 11 of 12 Date 6 June 2003
Time: 11:52 Pressure: 6.6 TOY! Time: 11:53 Pressure: 8 TOY! Time: 11:54 Pressure: 9 TOY! Time: 11:55 Pressure: 10.5 TOY! Time: 11:55 Pressure: 12 TOY! Time: 11:57 Pressure: 13.8 TOY! Time: 11:59 Pressure: 15 TOY! Time: 12:00 Pressure: 16.5 TOY! Time: 12:01 Pressure: 19.5 TOY! Signed: 4 Must Pekedi Witnessed:			
A. OP 770 (MBX1), OP xxx (MQX1): Lambda Plug Leak Install a "Rad-Lab" Tee to the Conflat Flange on the end of Connect one leg of the Tee to a pumping station through a V Convectron vacuum gauge on the other leg.	thje Conducto	or Protection Tu	be.
Make sure the Helicoflex flnage is opened to the atmosphere Evacuate the Conductor Protection Fube to about 20 mTorr. Close the Veeco valve and record the reading of the convects Allow the pressure to rise to about 10 Torr. Note: The trapped volume for MBX1 is 4.3 liter, so the rate of and the trapped volume for MQX1 is 8.3 liter, so the rate of pate: Date:	ron gage ever	10 mayat ha land	han 6.5 mTorr/sec, n 3.4 mTorr/sec.

Pressure:

Pressure:

Pressure:

Pressure:

Pressure:

Pressure:

Pressure:

Pressure:

Time:

Time:

Time:

Time:

Time:

Time:

Time:

Time:

Author

Jon Zbasnik

LH2003

XXXXXX

12 of 12

Department
Mechanical Engineering

Date

6 June 2003

essure:essure:
-

ENGINEERING NOTE

Cat. Code LH2004 Serial #

M20007

Page

14 of 15

Department

(draft7)

Date

Doyle Byford and Jon Zbasnik

Author

Mechanical Engineering

18 June, 2003

IX. DATA SHEETS FOR OPERATION 800 AND 810 TESTS

Data sheet for operation 800 test Assembly S/N 25I448-8

Conductor	Leakage, micro amps	Conductor	Leakage, micro amps	Conductor	Leakage, micro amps
	or		or	-	or
	Trip		Trip		Trip
	Voltage		Voltage		Voltage
5U	0	V3B	0.0	A3B	0,0
5L	0	V3A		A3A	1
8U	0	A4B		A2B	
8L	0	A4A		A2A	
B6B	0.0	B4B		H1B	
B6A		B4A		H1A	
ВЗВ		H2B		V1B	,
B3A		H2A		V1A	4
Н3В		V2B			
H3A	J	V2A	4		

Signed <u>Grandfarm</u> Date <u>9/25/03</u>
